



07.12.2024

TENNESSEE WINGS OF LIBERTY MUSEUM




Completed Work



Groundbreaking

- With 180+ attendees, the groundbreaking was a great success
- The Foundation hosted service men & women, civilian partners & businesses, government officials, and the entire project team

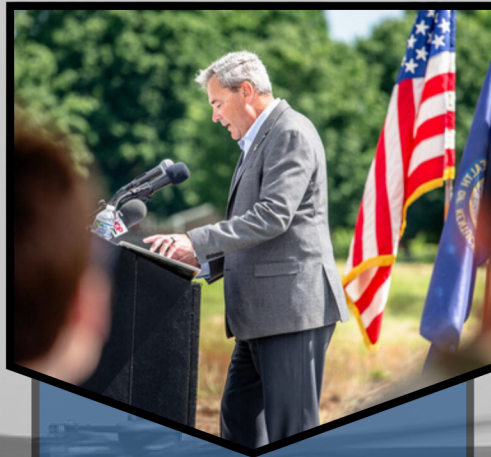

Demolition

- All required permits have been approved and all vegetation shown on the demo plan have been removed
- All asphalt shown on the demo plan has been removed & disposed



Site Work

- All storm water protection measures are in place and available for inspection
- The construction entrance has been graded and all soil remediation is complete

Current Work



- Paving scheduled for construction entrance
- Fencing contractor is preparing for installation of construction gate



- Rough grade for the exhibit hall is in progress
- Layouts for the footings will be completed after rough grade



- The construction managers office is onsite and being set up with utilities
- CM now has full-time onsite presence

Current Work

July

Concrete Mobilization

July

Footing Layout
& Excavation

August

Building Pad
Installation

