




10.04.2024

# TENNESSEE WINGS OF LIBERTY MUSEUM



## Current Work

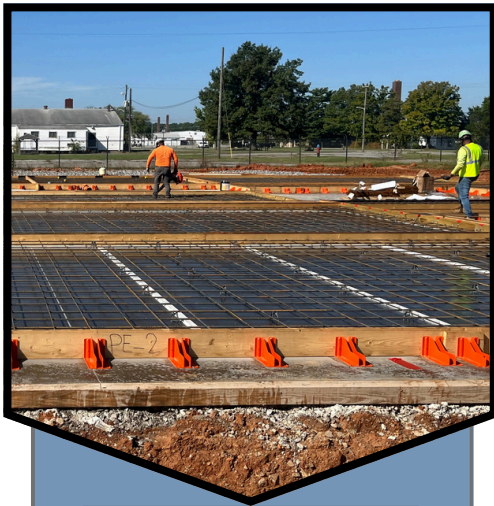


### Tilt Walls

- Rebar is being tied for the first set of tilt panels
- The forms are being cleaned and prepped for the upcoming pours



### Tilt Prep

- The crane for the tilt wall assembly has been coordinated with the FAA
- Crane delivery has been set up and will be assembled in the coming week

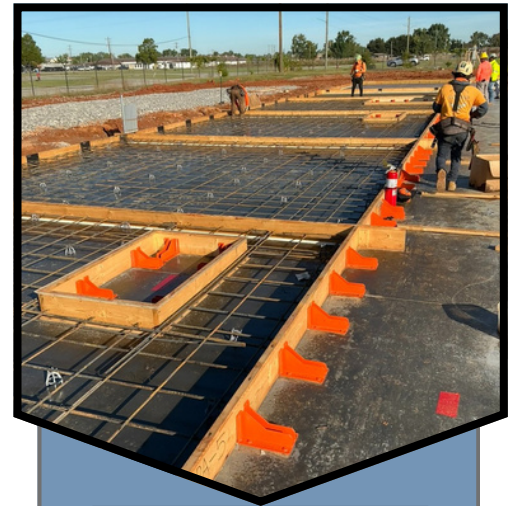

### Fabrication

- The structural submittals have all been reviewed and approved
- The subcontractor has begun work on steel fabrication so they can begin work on assembly pending the completion of the tilt walls

# Complete Work



- The entirety of the slab on grade has been completed and tested for flatness
- All formwork has been completed for the tilt panels



- The crane pad is completed and encompasses the East, South, and West of the slab on grade
- This provides a stable working platform for the crane during the tilt process



- The remaining storm water work has been completed
- The excavation and storm water scope is now complete on phase 1

# Upcoming Work

**October** Tilt wall forming & pours

**November** Tilt wall Erection

**December** Roof construction begins

