




10.18.2024

TENNESSEE WINGS OF LIBERTY MUSEUM




Current Work

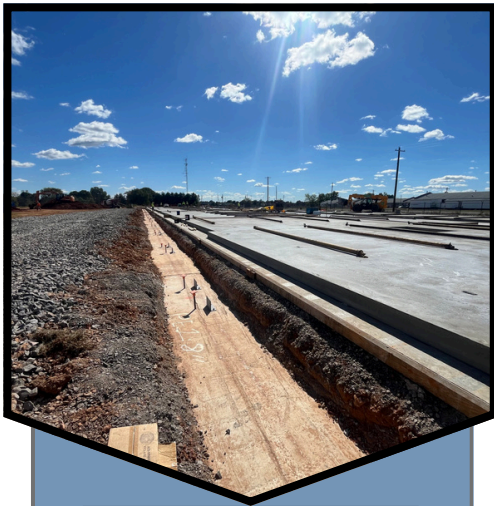


Crane Operations

- The revised crane operation plan has been approved and the delivery and assembly is scheduled
- The site will be closed to tours for the duration of this work

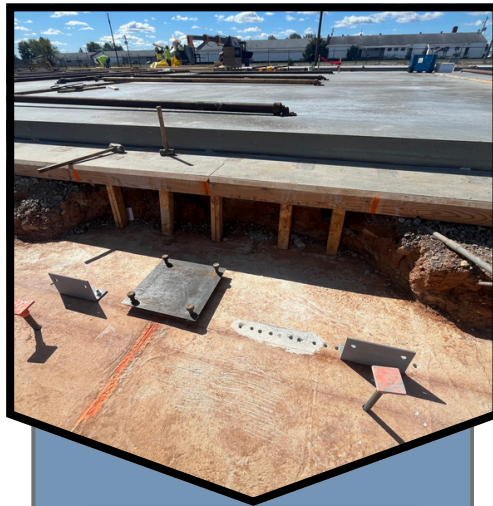

Tilt Prep

- The pick points in the tilt walls have been located, cleaned, and prepped
- The angle iron bracings have been anchored into the building footing

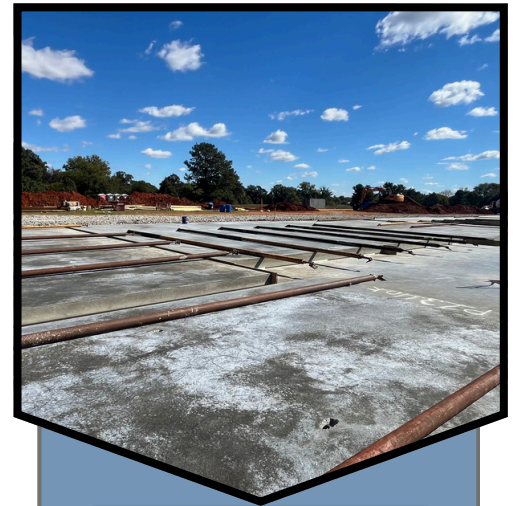

Shoring

- The steel bracing bars have been anchored into the tilt walls
- This shoring will stay in place until the trusses & structural columns are installed

Complete Work



- 1) The location of the TNWOL Building pad prior to ground breaking
- 2) The location of the TNWOL Building pad after grading and prior to the slab on grade
- 3) The slab on grade & tilt walls prior to wall erection

Upcoming Work

October

Tilt wall Erection

November

Steel Erection

December

Roof construction begins

