



TENNESSEE  
WINGS OF LIBERTY  
MUSEUM

11.27.2024



## Current Work




### Roofing

- Roofing materials are being delivered
- The roof decking is being inspected by the certified weld inspector
- All roofing related sub-contractors are onsite and have begun work



### Mechanical

- The trench for all mechanical piping has been dug and the required pipes are being fused and set
- The required conduit for mechanical controls are being run into the building

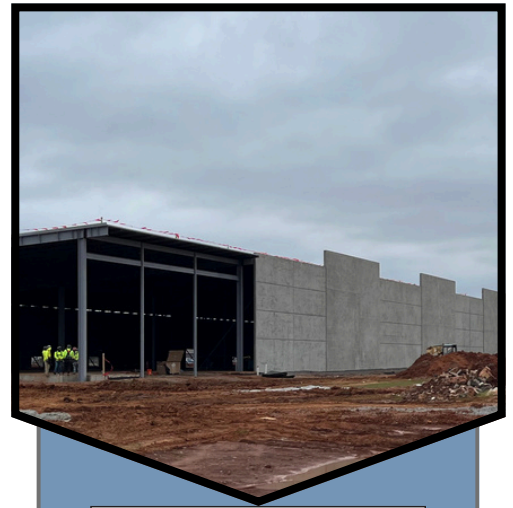

### Concrete

- The subcontractor in charge of the caulk is onsite and has begun work on the interior and exterior
- The panels have been cleaned and the stain will be applied shortly

# Complete Work



- 1) All roof decking has been hung and anchored
- 2) All panels have been power washed in preparation for caulk and stain
- 3) All structural steel components have been reviewed by the structural engineer and architect

HAPPY  
THANKSGIVING  
FROM THE TENNESSEE WINGS OF LIBERTY  
MUSEUM PROJECT TEAM!



Prepared by Commonwealth Development Group, Inc.
