




12.20.2024

TENNESSEE WINGS OF LIBERTY MUSEUM



Current Work

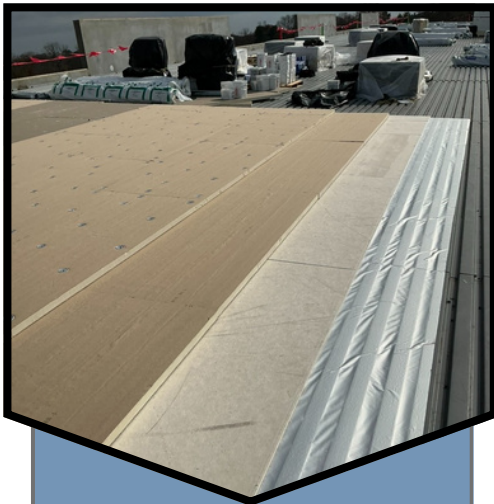

Roofing

- Roofing layers consisting of densdeck, air & vapor barrier, and Ethylene propylene diene monomer are being installed
- The EPDM adhesive is being scheduled based on weather to ensure longevity



Mechanical



- Backfill of the mechanical piping trenches is underway
- Once complete, grading for the west and north sections of the property will begin



Framing

- Insulation panels are being adhered to the tilt-up panels
- The framers will begin work on their metal stud framing once this is complete

Complete Work

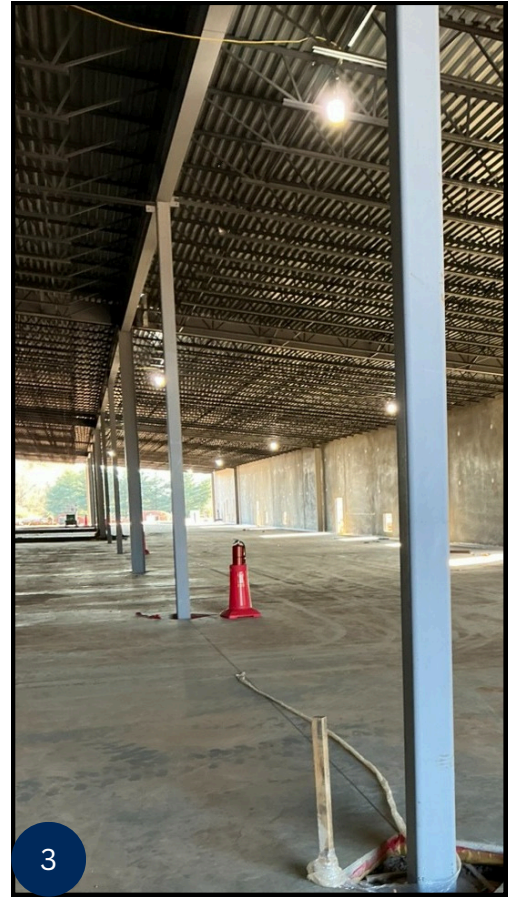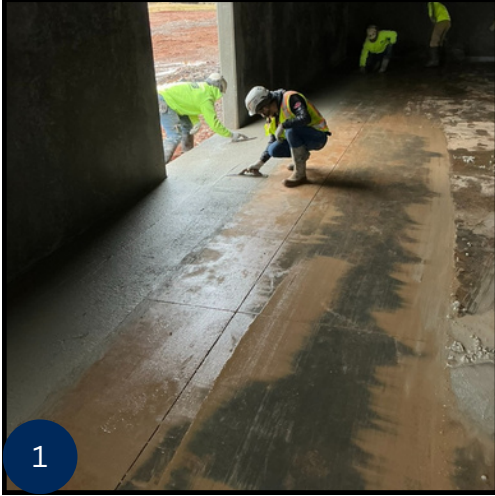

- 1) The 3' concrete pour back has been completed meaning the slab construction is done in its entirety
- 2) All mechanical piping has been run into the building
- 3) All tilt wall braces have been removed and temp lighting has been installed

Upcoming Work

December EPDM Roofing Installation

January Framing & Insulation

January Utility Connections

