




1.03.2025

# TENNESSEE WINGS OF LIBERTY MUSEUM




## Current Work

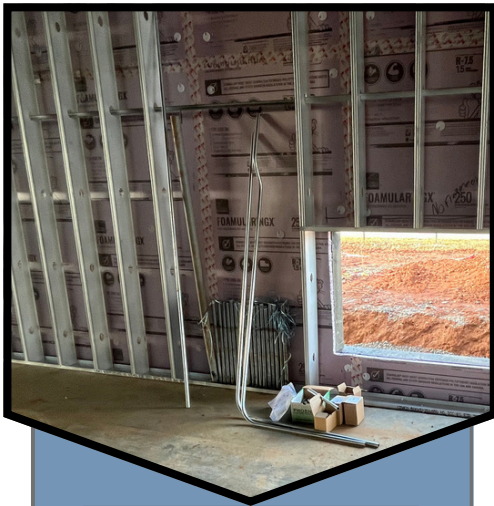


### Electrical

- The electricians & low voltage contractor have begun running all pathways for wall receptacles and data points
- The IDF cabinet conduits are stubbed up and ready for the cabinet install

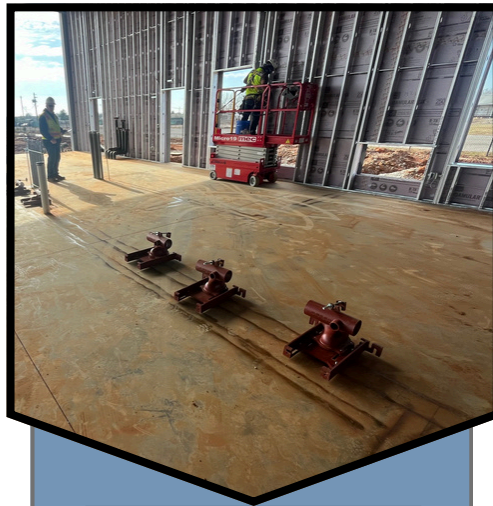

### Mechanical

- Fire suppression hangers are being installed overhead in preparation for the piping
- Fire suppression system valves are being delivered in preparation for connections

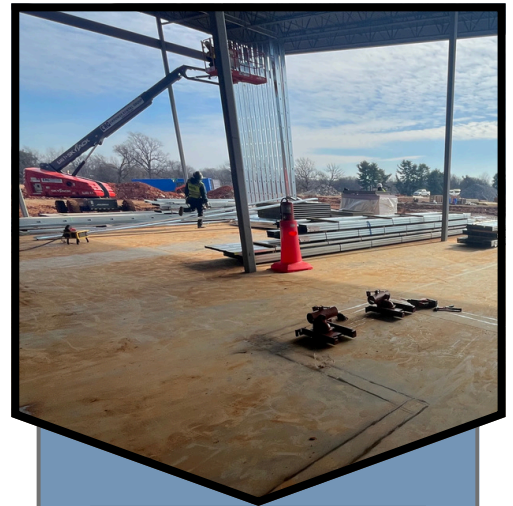

### Framing

- Metal stud framing at the entrance continues
- Layouts for the interior rooms are complete and interior wall framing in the lobby has begun
- Coordination is underway for the built-in displays

# Complete Work



- 1) All framing and insulation is complete along the tilt- up walls
- 2) The EPDM roofing is complete including all penetrations
- 3) All exterior caulk and waterproofing is complete

# Upcoming Work

**January** Framing & Insulation

**February** Plumbing Equipment Installation

**February** Electrical Equipment Installation

