




TENNESSEE  
WINGS OF LIBERTY  
MUSEUM

1.24.2025




## Current Work

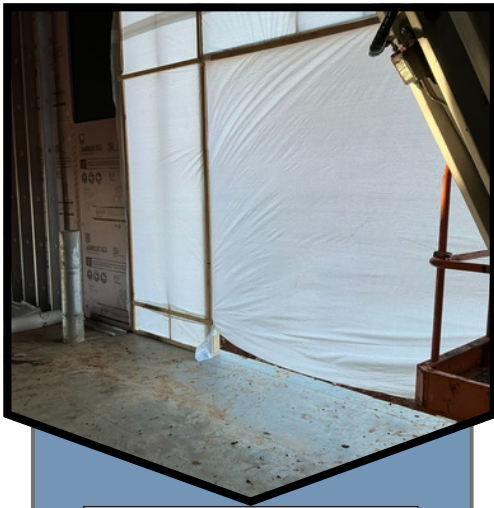

### Enclosure

- The overhead door entrance, pedestrian doors, pass through to Phase 2A have been temporarily
- The main exhibit hall can now be temporarily heated for interior work to be completed

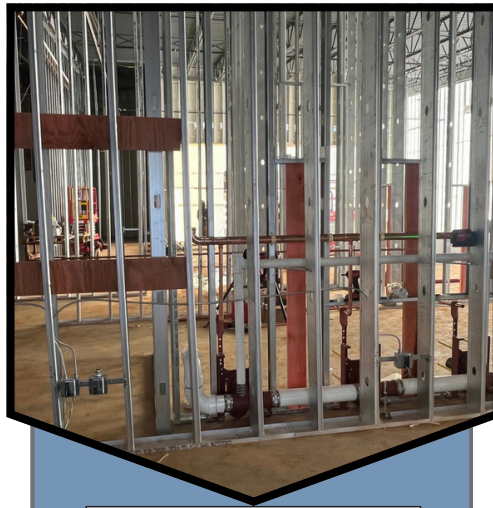

### M.E.P

- Fire suppression piping is being run throughout the exhibit hall
- Plumbing for the restrooms in the lobby is being installed
- The rough-ins for electrical has begun



### Framing

- Sheetrock installation is beginning on walls down the interior of the main exhibit hall
- The chronology walls running down the center of the main exhibit hall are being framed

# Complete Work



- 1) The Historical Foundation, CDG, members of the 160th, 5th group, and the 101st met to discuss the museum layout
- 2) All Framing in the lobby is complete
- 3) The main entrance has been temporarily enclosed - now site visitors can walk through what will be the future main entrance

# Upcoming Work

**January** Overhead Electrical Rough-in

**February** Sheetrock for Interior Walls

**February** Electrical Equipment Installation

