



TENNESSEE
WINGS OF LIBERTY
MUSEUM

2.21.2025




Current Work



Mechanical

- Ductwork is continuing to be hung in the lobby and offices
- The supply and return structures for the exhibit hall ductwork have been delivered and is scheduled for install

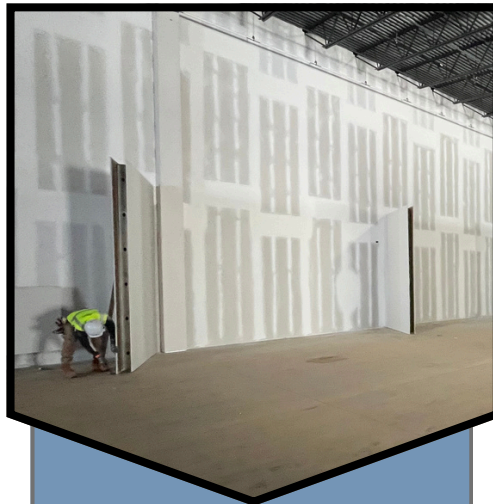

Drywall


- The angled alcove walls to accommodate exhibits are almost complete with dry wall
- The interior walls of the lobby, offices, and restrooms will continue to have drywall hung



Plumbing

- Work in the riser room continues now that the main sprinkler pipe and branches have been hung
- Copper water lines in the restrooms are being tested and insulated.

Complete Work

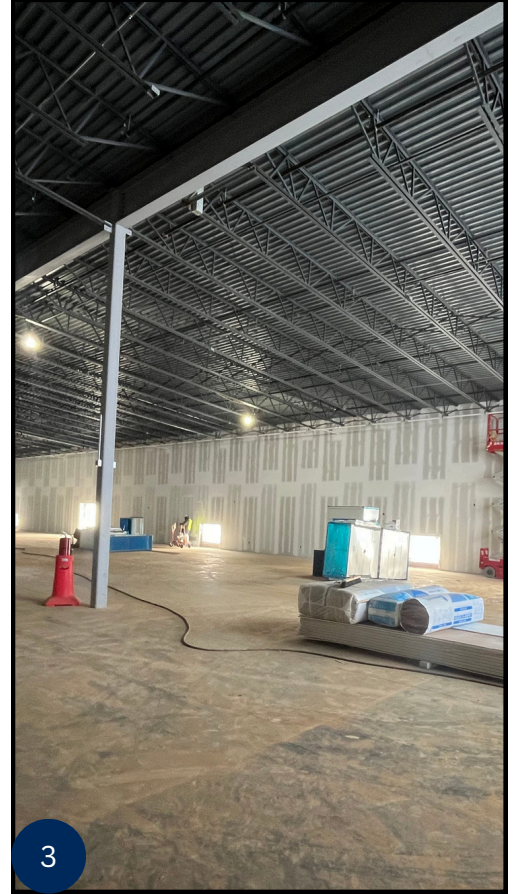

- 1) The center line chronology walls are complete and ready for paint
- 2) Fluid applied waterproofing is complete at the main entrance
- 3) Overhead electrical rough-in's are complete

Upcoming Work

February Ductwork Installation

March AV Data Cabling

March Interior Paint Begins

