



TENNESSEE
WINGS OF LIBERTY
MUSEUM

3.28.2025



Current Work




Exterior

- Glass has been delivered and installation is in progress at the main entrance
- The metal panels for the main entrance walls have been accepted and installation has begun



M.E.P

- Supply and return ducts are being installed in the main exhibit hall
- The overhead rigid ductwork is being insulated and will be painted to match the ceiling
- Underground water & sewer is set for install

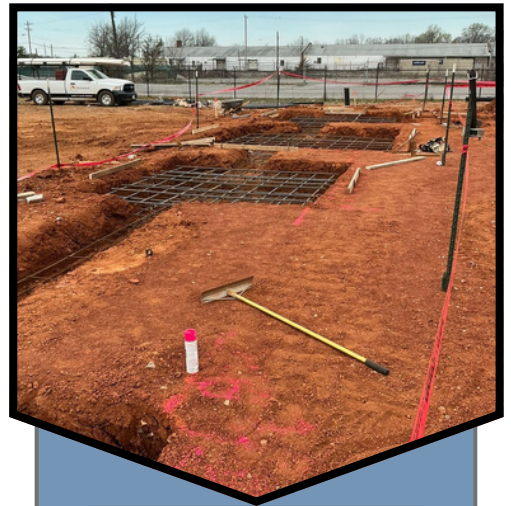

Footings

- The site for the atrium has passed all geotechnical testing and excavation has begun
- Rebar cages have been tied and set in preparation for concrete

Complete Work



- 1) The museum's gas connection has been made which is a critical part of the mechanical systems
- 2) The data cables have been run from our IDF cabinet to our floor boxes on the north side of the main exhibit hall
- 3) The main switchboard has been installed

Upcoming Work

April Glass at Storefront

April Atrium Footings

April Slab prep for Atrium

