



09.06.2024

# TENNESSEE WINGS OF LIBERTY MUSEUM




## Current Work



### Footings

- The continuous footer at the building perimeter is being excavated, tied and poured
- This is the footer the tilt panels will sit on top of

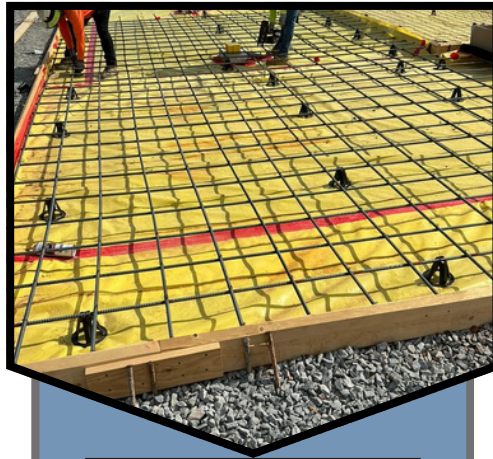

### Slab on Grade

- Forming and rebar work continues for the thickened slab section and remaining regular slab section



### Electrical

- Floor boxes are being prepped for upcoming slab on grade pours
- Electrical conduit for all rooms outside of the main exhibit hall is being run

# Complete Work



- Phase 1 of the slab on grade pour for the main exhibit hall has been completed
- All inspections of the concrete have been reviewed and approved



- The storm water lines have been installed to the west and south of the building
- The structure to the north have been approved and purchased



- Plumbing for the lobby area has been run and stubbed up in preparation for the slab on grade in that location

# Upcoming Work

**September** Column Line Footer Pours

**September** Continuous Footer Excavation

**September** Slab-on- Grade phased pours begin

